LAB — Agile Workflow in Jira for SilverTrust

Reflection & Screenshots Document

Part 1 — Reflection

1. How did you translate stakeholder pain points into epics?

The starting point was the pain point discovery report from Lab 1, which documented four personas: Rachel Kim (Client Success), Emmanuel Patel (Account Management), Carolina Nami (CEO), and Carlos (Technical Specialist). Instead of creating one epic per persona, I looked for recurring themes across all interviews.

Three clear functional clusters emerged:

1) the need for unified, aggregated client data from multiple platforms shared by Rachel and Emmanuel;
2) the need for AI-powered automation to reduce manual prep and improve response times shared by Emmanuel and Carolina;
3) the need for cross-platform search and knowledge management, the core pain point of Carlos. Each cluster became an Epic:

Epic	Problem solved	Stakeholders
EPIC-01: Unified Client Data Aggregation	Fragmented data across CRM, email, Slack — search takes 30+ min	Rachel Kim, Emmanuel Patel
EPIC-02: AI Communication & Automation	30-40 min manual prep per call; 24h response times; low satisfaction scores	Emmanuel Patel, Carolina Nami
EPIC-03: Cross-Platform Search & Knowledge	Slack unarchived; no cross-tool search; knowledge lost between projects	Carlos

2. What was challenging about writing user stories?

The main challenge was the level of specificity. The temptation was to write vague stories like "improve data access", which sound useful but cannot be tested or estimated.
Writing in the format "As a [stakeholder], I want [feature], so that [benefit]" forced a useful discipline: every story had to be anchored to a real person and a real outcome.

A second challenge was scoping: some pain points were broad enough to become entire epics. For example, "cross-platform search" could have been one story or five. I resolved this by asking: can this be built and tested independently in one sprint? If not, it was split into smaller stories.

Finally, writing acceptance criteria that are specific and testable — not just descriptive — required thinking ahead to implementation. Criteria like "search returns results in under 5 seconds" are verifiable; "the search should be fast" is not.

3. How did you prioritize your backlog?

Prioritisation followed three criteria in order of importance:

1. Technical dependency: stories that are prerequisites for others were elevated to Highest. Without the unified dashboard (UCIPS-5) and CRM sync (UCIPS-6), no other story has real data to work with.

2. Business impact: stories addressing the most acute pain points received higher priority. The CEO's satisfaction score concern and Carlos's complete inability to search across platforms were classified as Highest.

3. Category: category 1 stories (n8n automation, API integrations) were generally prioritised before Category 2 (AI/LLM features) because AI features depend on clean, connected data being available first.

One adjustment made during review: UCIPS-8 (AI pre-call briefs) was initially Highest but revised to High, because while valuable it does not block other work. UCIPS-9 (sentiment analysis) was upgraded from Medium to High and moved to Sprint 2 because the CEO's KPI — client satisfaction >= 4.3/5 — is a core project success metric.

4. What questions or assumptions did you make?

Sprint duration: I assumed 2-week sprints, typical for a Scrum team. For an Ironhack lab context the actual delivery is compressed, but the structure reflects real-world planning.

Story point estimates: no estimates were assigned because the team size and velocity are unknown at this stage. In a real project, the team would run a planning poker session before committing to sprint contents.

Data sources: The epics assume SilverTrust's data lives in a CRM, Slack, and email. If other platforms exist (e.g., a project management tool, a proprietary database), additional stories would be needed for EPIC-01.

Stakeholder availability: acceptance criteria include response time thresholds (e.g., "<4 hours", "<5 minutes"). These were derived from the project brief KPIs and assumed to reflect real SLAs agreed with the client.

Sprint 3 as buffer: after moving UCIPS-9 to Sprint 2, Sprint 3 was left empty intentionally — a conscious decision to reserve capacity for stories discovered during Sprint 1 and 2 reviews, bug fixes, or scope changes requested by stakeholders.

Part 2 — Jira Screenshots

The following screenshots document the final Jira configuration for project UCIPS (jessicadipasquale.atlassian.net). Add your screenshots in the placeholders below.

Screenshot 1 — Epic View

All three epics visible with their descriptions.

Work	Status	Due date	Priority	Assignee	Comments
UCIPS-1 Unified Client Data Aggregation	TO DO	None	Medium	Unassigned	Add comment
UCIPS-2 AI-Powered Communication and Automation	TO DO	None	Medium	Unassigned	Add comment
UCIPS-4 Risk and Health Monitoring Dashboard	TO DO	None	Medium	Unassigned	Add comment

Screenshot 2 — Backlog View

Full backlog showing Sprint 1 (5 stories), Sprint 2 (4 stories), and empty Sprint 3.

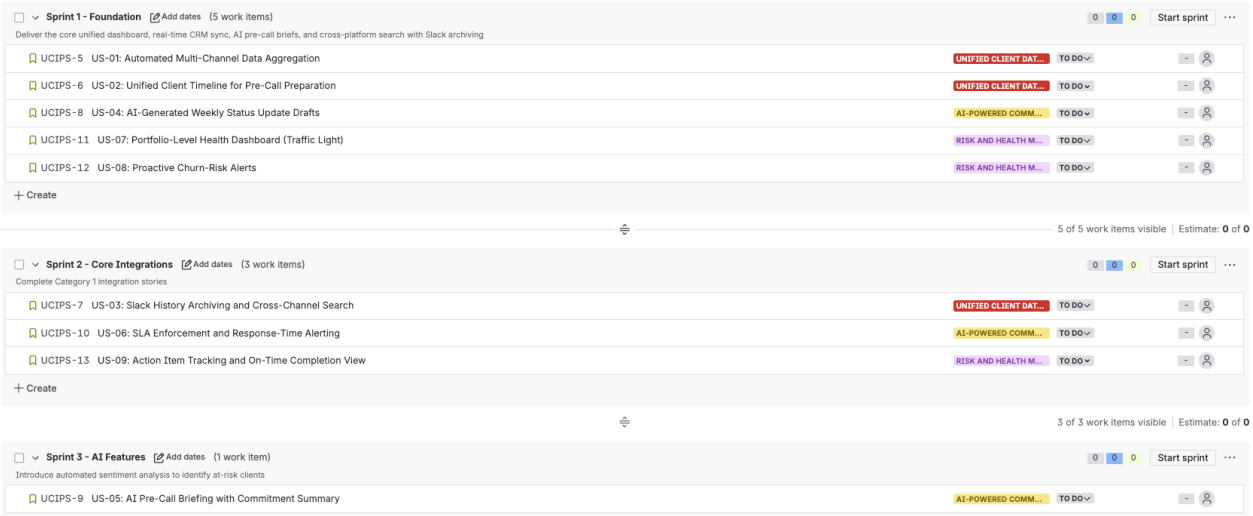

Screenshot 3 — Board View

Scrum board showing

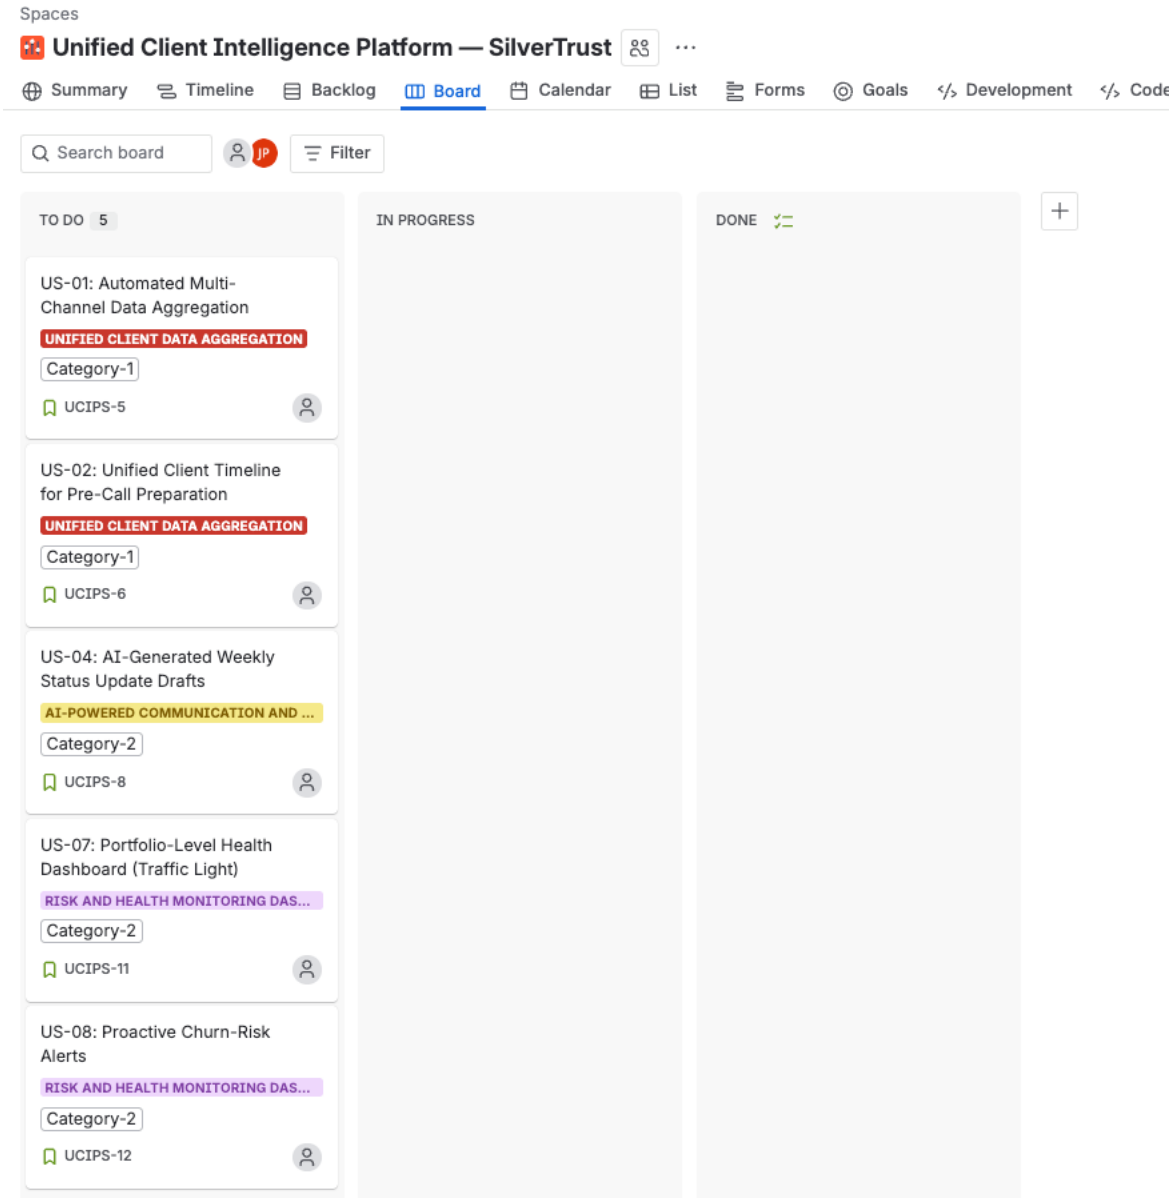

sprint structure and columns (To Do / In Progress / Done).

Screenshot 4 — User Story Detail

One user story open showing acceptance criteria, epic link, priority and label.

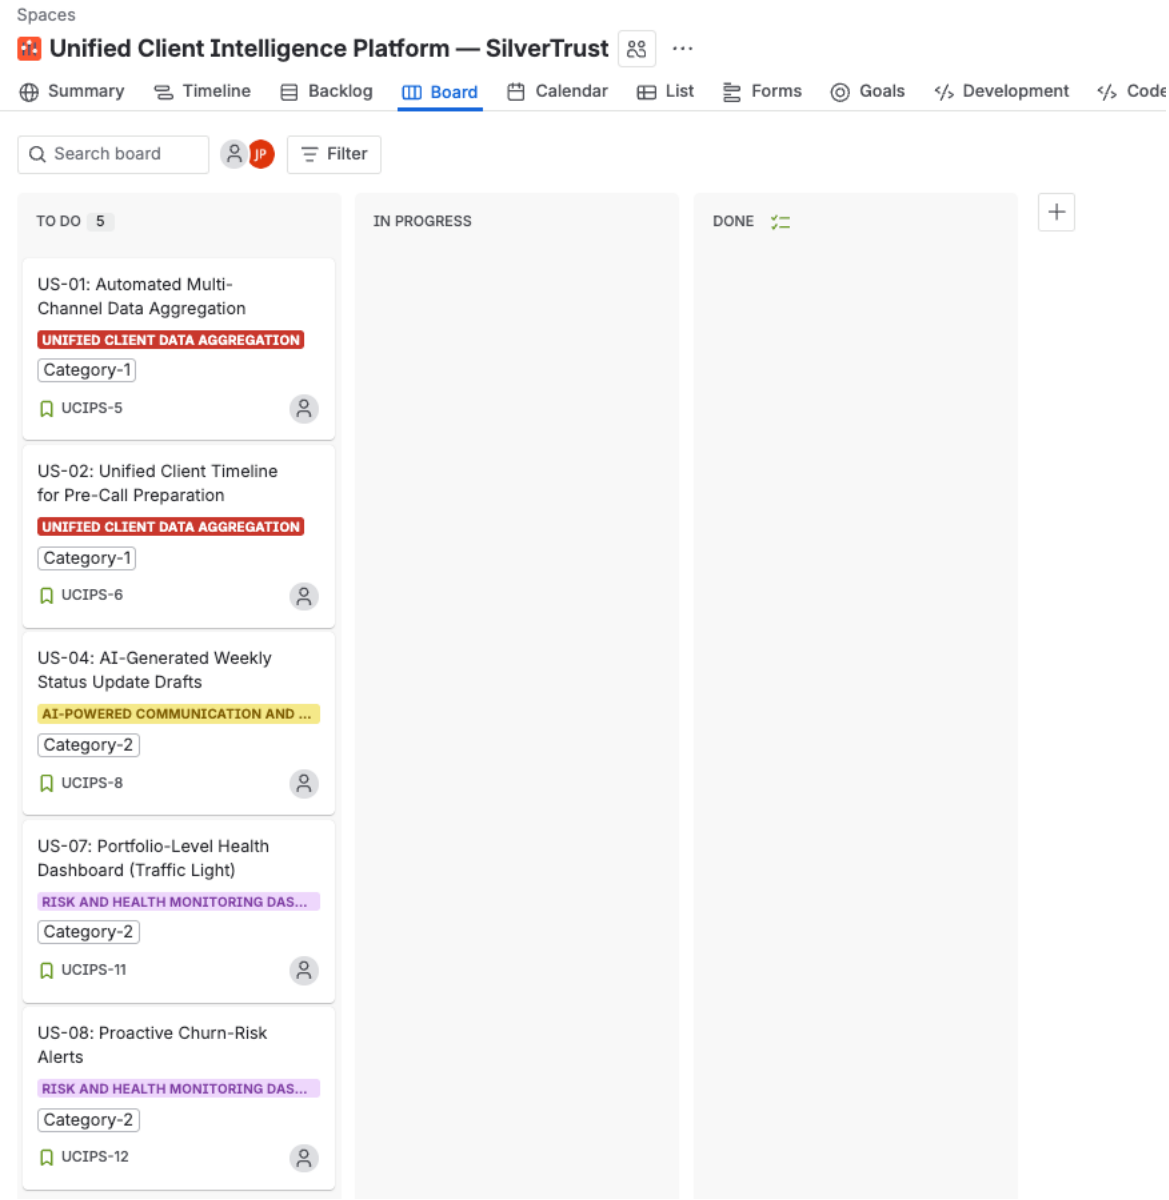

Part 3 — Project Summary

The UCIPS Jira project for SilverTrust translates four stakeholder pain points into three epics and nine user stories distributed across two active sprints.

EPIC-01 (Unified Client Data Aggregation) addresses Rachel Kim and Emmanuel Patel's need for a single source of truth, replacing 30+ minutes of manual data gathering with an automated, searchable dashboard. EPIC-02 (AI Communication & Automation) targets Emmanuel's pre-call prep burden and Carolina Nami's declining satisfaction scores, introducing AI-generated briefs and smart email triage. EPIC-

03 (Cross-Platform Search & Knowledge) solves Carlos's inability to search across Slack, email, and CRM, creating a unified knowledge layer for the whole team.

Sprint 1 (Foundation) delivers the five Highest-priority stories that form the technical backbone. Sprint 2 (Core Integrations) completes the remaining four High-priority stories. Sprint 3 is reserved as a buffer for scope adjustments or newly discovered requirements.
